




City of Lowell

Lowell High School Project

Owner's Project Manager

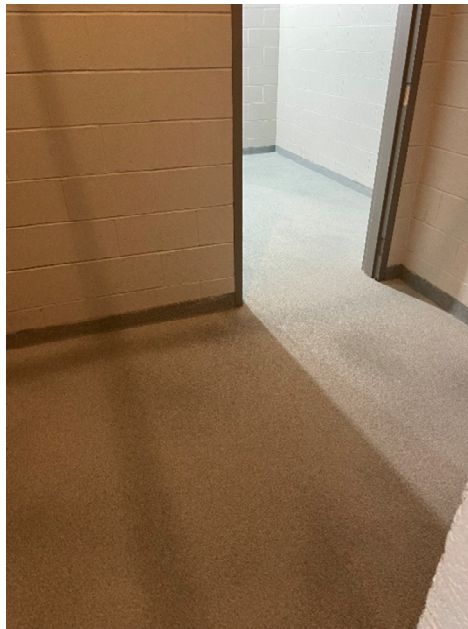

MSBA Monthly Report

Contents:

1. Progress Report
2. Cash Flow
3. Project Schedule
4. MSBA ProPay PTD
5. PCO Log

Skanska USA Building, Inc**Jim Dowd****Progress Report as of Date 4/30/2022**

District Name	Lowell	MSBA ID	201401600505
School Name	Lowell High	Project Name	
OPM Firm Name	Skanska USA Building, Inc	School Building Committee Representative	Thomas Golden
Project Director	Jim Dowd	Total Project Budget (ProPay)	\$343,399,220
Designer Firm Name	Perkins Eastman/DPC	Encumbered (Reporting Period)	\$0
Principal	Joseph S Drown	Encumbered (to Date)	\$248,918,608
General Contractor Firm Name	Suffolk Construction Company	Total Project Invoices Received (to Date)	\$72,725,253
General Contractor Contact Name	Jeffrey A Gouveia	Project Completion Percentage	26%

OPM**Skanska USA Building, Inc****Progress Report as of Date 4/30/2022****Contract Summary**

Original Contract Amount	\$458,760
Contract Amendments (to Date)	2
Value of Contract Amendments (to Date)	\$9,006,810
Total Contract Amount	\$9,465,570
Contract Amendments as Percentage of Original Contract Amount	1,963.3%

Payment Summary

Total Contract Amount	\$9,465,570
Invoices Paid (to Date)	\$3,405,597
Invoices Received (Reporting Period)	\$134,580
Contract Amount Remaining	\$5,925,393

OPM Activities (Reporting Period)

The Final GMP is anticipated to be submitted next month. Weekly PCO meetings are ongoing with continued daily review. The PCO log and Budget are consistently maintained. There is regular review and feedback on invoices and PCOs. Review and supervision of both the daily construction schedule and the overall project schedule continues. Coordination with FFE and Move Management is ongoing. Weekly Move Management meetings continue. The OPM's field staff complete daily reports with photos. Monthly requisitions are reviewed and processed in a timely manner. Daily problem solving with the Project Management team is ongoing. The City Managers Office and the School Building Committee are kept up to date on progress

Project Budget Status

GMP is being finalized with Suffolk and increased funding approved by City will be added at PFA Bid Amendment submission. Perkins Eastman and Skanska received no additional fee with the project budget increase and Suffolk received no additional General Conditions.

MSBA Closeout Status

n/a

Potential Issues

Supply chain issues continue to be addressed by the Project Team. Material cost increases from Trade Partners for cost increases are declined as cost increase changes are not part of the Trade Partners' contracts.

DESIGNER**Perkins Eastman/DPC****Progress Report as of Date 4/30/2022****Contract Summary**

Original Contract Amount	\$1,095,000
Contract Amendments (to Date)	9
Value of Contract Amendments (to Date)	\$26,174,816
Total Contract Amount	\$27,269,816
Contract Amendments as Percentage of Original Contract Amount	2,390.4%

Payment Summary

Total Contract Amount	\$27,269,816
Invoices Paid (to Date)	\$20,681,557
Invoices Received (Reporting Period)	\$125,813
Contract Amount Remaining	\$6,462,446

MBE/WBE

MBE Percentage	6.0%
MBE Actual	3.2%
WBE Percentage	9.0%
WBE Actual	5.2%

Workforce Participation

Total Hours	1,016
Minority Hours	2
Minority Percentage	1.0%
Minority Workforce Participation	0.0%
Female Hours	556
Female Percentage	55.0%
Female Workforce Participation	0.0%

RFIs and Submittals

RFIs Issued (Reporting Period)	58	
Total RFIs Issued (to Date)	583	
Remaining Open RFIs – Past 30 Days	3	
Notes		
Remaining Open RFIs – Past 60 Days	0	
Notes		
Remaining Open RFIs – Past 90 Days	0	
Notes		
Submittals Received (Reporting Period)	23	
Total Submittals Received (to Date)	972	
Submittals Reviewed (Reporting Period)	48	
Total Submittals Reviewed (to Date)	1,209	
Comments (Remaining Open Submittals)	Process is progressing along well. AE, Consultants and CM continue to coordinate on required expedited reviews.	
Phase	Construction	Phase Scheduled Completion Date 7/1/2026
Designer Activities (Reporting Period)	Requisitions (monthly) and Meeting Minutes (weekly) are responded to timely. Field bulletins are being reviewed and quantified in submittals and RFIs. Continues to actively review submittals. Phasing coordination is ongoing/ Monthly and weekly inspections are conducted by AE and consultants. Onsite problem solving with OPM & CM teams.	
30 Day Look Ahead	Weekly inspections continue along with Field Bulletins being issued and Submittals and RFIs being reviewed.	
Commissioning Consultant	BR+A	
Commissioning Consultant Status	Working with Project Team on the startup and testing plan	

GENERAL CONTRACTOR Suffolk Construction Company**Progress Report as of Date 4/30/2022****Contract Summary**

Original Contract Amount (including CM-At-Risk Amendments)	\$800,000
Change Orders (to Date)	8
Value of Change Orders (to Date)	\$209,996,844
Total Contract Amount	\$210,796,844
Procurement Type	CM-at-Risk
Change Orders as Percentage of Original Contract Amount	26,249.6%
Pending Change Orders	\$0
Change Order Status	PreGMP 9 - Final development almost complete

Payment Summary

Total Contract Amount	\$210,796,844
Invoices Paid (to Date)	\$42,439,744
Invoices Received (Reporting Period)	\$3,525,984
Contract Amount Remaining	\$164,831,116

MBE/WBE

MBE Percentage	5.0%
MBE Actual	4.7%
WBE Percentage	5.0%
WBE Actual	8.3%

Workforce Participation

Total Hours	97,057
Minority Hours	21,902
Minority Percentage	22.6%
Minority Workforce Participation	15.3%
Female Hours	2,682
Female Percentage	2.8%
Female Workforce Participation	6.9%

Schedule Assessment

Notice to Proceed Date	3/2/2021
Physical Progress	18%
Substantial Completion Date (Reported)	5/4/2026
Substantial Completion Date (Contract)	7/1/2026
Substantial Completion Date (Certificate)	7/1/2026
Construction Progress (Reporting Period)	Continuing with major mechanical tie-ins. Gym equipment install wrapping up. Flooring prep continues and finish floor beginning in some areas. Exterior wall panel installation has commenced. Painting on Level 1 & Level 2 finishing up. Ceiling grid install continues on Level 1 with panel install following in sequence. Shower room and stairwell wall tile install is under way.
30 Day Look Ahead	Continued work on ceiling, flooring and finishes installation. Wrapping up of mechanical tie ins. Continuation of exterior wall panels. Exterior planters, stairs and ramps construction to commence.
Overall Schedule Assessment	On schedule per Suffolk
Problems Identified (Schedule or Construction)	Suffolk working diligently to better current delivery date of bleachers of late August.
Quality Control	QA/QC items are actively reviewed, addressed and closed out.
Safety Compliance	Acceptable
Number of Claims (to Date)	0
Value of Claims (to Date)	\$0
Comments	n/a
Recorded Manpower (Reporting Period)	Average 75 workers per day
Contractor Closeout Status	Continued efforts on closeout of Phase 1 trade partners who are only associated with Phase 1 work.


Certification

The undersigned hereby certifies that, to the best of his/her knowledge, the information contained in this monthly report and attached hereto are true and accurate.

Project Director/Project Manager

James A. Board II

Print Name



Signature

5/12/22

Date

ProPay Cost Code Categorization

April-22
The City of Lowell
Lowell High School Project
Lowell, MA

Narrative:

The table below outlines the cost of all invoices for the month of **April 2022** arranged into the ProPay categories, see attached.

Summary Table of Invoices:

			Totals:	\$ 3,806,363.05	\$ 176,299.24	\$ 3,630,063.81
Company	Invoice Number	Cost Code & Description	Invoice Amount	Retainage	Pay This Amount	
Perkins Eastman	67151.00.0-35	0201-0700 - A&E - Construction Contract Administration	\$ 125,813.30	\$ -	\$ 125,813.30	
Skanska USA Building Inc.	1316824-000-14730-65	0102-0700 - OPM - Construction Contract Administration	\$ 134,580.00	\$ -	\$ 134,580.00	
Suffolk Construction	Req. 19	0502-0100 - Division 1 - General Requirements	\$ 84,332.72	\$ 4,216.64	\$ 80,116.08	
Suffolk Construction	Req. 19	0502-0010 - GMP - Fee	\$ 96,738.34	\$ 4,836.92	\$ 91,901.42	
Suffolk Construction	Req. 19	0502-3100 - Division 31 - Earthwork	\$ 11,562.00	\$ 578.10	\$ 10,983.90	
Suffolk Construction	Req. 19	0502-0300 - Division 3 - Concrete	\$ 74,301.00	\$ 3,715.05	\$ 70,585.95	
Suffolk Construction	Req. 19	0502-0500 - Division 5 - Metals	\$ 98,467.35	\$ 4,923.37	\$ 93,543.98	
Suffolk Construction	Req. 19	0502-0700 - Division 7 - Thermal and Moisture Protection	\$ 94,070.00	\$ 4,703.50	\$ 89,366.50	
Suffolk Construction	Req. 19	0502-2100 - Division 21 - Fire Suppression	\$ 19,775.00	\$ 988.75	\$ 18,786.25	
Suffolk Construction	Req. 19	0502-2600 - Division 26 - Electrical	\$ 608,422.53	\$ 30,421.13	\$ 578,001.40	
Suffolk Construction	Req. 19	0502-0400 - Division 4 - Masonry	\$ 68,035.00	\$ 3,401.75	\$ 64,633.25	
Suffolk Construction	Req. 19	0502-2200 - Division 22 - Plumbing	\$ 55,200.00	\$ 2,760.00	\$ 52,440.00	
Suffolk Construction	Req. 19	0502-2300 - Division 23 - HVAC	\$ 650,178.00	\$ 32,508.90	\$ 617,669.10	
Suffolk Construction	Req. 19	0502-0900 - Division 9 - Finishes	\$ 614,206.90	\$ 30,710.35	\$ 583,496.56	
Suffolk Construction	Req. 19	0502-1100 - Division 11 - Equipment	\$ 660,073.37	\$ 33,003.67	\$ 627,069.70	
Suffolk Construction	Req. 19	0502-0800 - Division 8 - Openings	\$ 378,122.54	\$ 18,906.13	\$ 359,216.41	
Suffolk Construction	Req. 19	0502-0600 - Division 6 - Woods, Plastics and Composites	\$ 12,500.00	\$ 625.00	\$ 11,875.00	
Universal Testing Services (UTS)	99423	0602-0000 - Testing Services	\$ 3,710.00	\$ -	\$ 3,710.00	
STV DPM	90024377	0699-0000 - Other Project Costs	\$ 16,275.00	\$ -	\$ 16,275.00	

INVOICE SUMMARY			
Invoiced to Date	Paid to Date	Percent Complete	Amount Remaining
\$ 555,529.00	\$ 555,528.82	99.99%	\$ 31.18
\$ 1,621,298.00	\$ 1,621,297.83	99.91%	\$ 1,386.17
\$ 399,179.00	\$ 399,178.96	99.46%	\$ 2,166.04
\$ 7,335.00	\$ 7,335.45	35.95%	\$ 13,071.55
\$ 2,583,341.00	\$ 2,583,341.06	99.36%	\$ 16,659.90
\$ 729,750	\$ 729,750	100.00%	\$ -
\$ 1,244,505	\$ 1,244,505	100.00%	\$ -
\$ 477,080	\$ 477,080	100.00%	\$ -
\$ 553,315	\$ 409,410	8.62%	\$ 5,654,170.00
\$ 0	\$ 0	0.00%	\$ 271,190.00
\$ 0	\$ 0	0.00%	\$ -
\$ 0	\$ 0	0.00%	\$ -
\$ 0	\$ 0	0.00%	\$ -
\$ 0	\$ 0	0.00%	\$ -
\$ 0	\$ 0	0.00%	\$ -
\$ 0	\$ 0	0.00%	\$ -
\$ 2,984,650	\$ 2,860,745	33.50%	\$ 5,925,360.00
\$ 6,256,000	\$ 6,256,000	100.00%	\$ -
\$ 8,758,400.00	\$ 8,758,400	100.00%	\$ -
\$ 1,751,680.00	\$ 1,751,680	100.00%	\$ -
\$ 1,317,433.30	\$ 1,198,271	17.55%	\$ 6,189,767.00
\$ -	\$ 0	0.00%	\$ 750,720.00
\$ 13,321.00	\$ 13,321	6.01%	\$ 208,461.00
\$ 18,096,834.62	\$ 17,977,672.62	71.68%	\$ 7,148,948.00
\$ -	\$ -	0.00%	\$ -
\$ 47,098.10	\$ 47,098.10	62.80%	\$ 27,902.00
\$ 82,019.45	\$ 82,019.45	21.03%	\$ 307,981.00
\$ 276,879.00	\$ 276,879.00	67.57%	\$ 132,871.00
\$ 248,877.00	\$ 248,877.00	65.65%	\$ 130,213.00
\$ 15,840.00	\$ 15,840.00	77.46%	\$ 4,610.00
\$ -	\$ -	0.00%	\$ 35,000.00
\$ 19,346.31	\$ 19,346.31	24.18%	\$ 60,654.00
\$ 690,059.86	\$ 690,059.86	49.67%	\$ 699,230.00
\$ 795,476.00	\$ 795,476.00	99.43%	\$ 4,524.00
\$ 1,046,039.37	\$ 927,372.34	17.61%	\$ 4,893,961.00
\$ 4,407,535.37	\$ 4,281,488.00	79.43%	\$ 1,141,471.00
\$ -	\$ -	0.00%	\$ 6,285,237.00
\$ 2,389,208.00	\$ 2,237,677.72	12.11%	\$ 17,347,401.00
\$ 925,962.00	\$ 925,962.00	6.16%	\$ 14,116,132.00
\$ 1,975,854.00	\$ 1,693,543.00	20.42%	\$ 7,698,593.00
\$ 3,031,830.00	\$ 2,970,895.00	35.24%	\$ 5,572,527.00
\$ 4,049,568.24	\$ 3,930,244.99	23.53%	\$ 13,157,878.00
\$ 81,046.00	\$ 12,500.00	3.22%	\$ 2,691,249.00
\$ 2,396,348.00	\$ 989,242.00	28.59%	\$ 5,986,694.00
\$ 986,370.13	\$ 797,299.66	3.79%	\$ 25,010,755.00
\$ 3,400,916.95	\$ 3,123,978.90	9.67%	\$ 31,765,696.00
\$ 380,970.00	\$ 380,970.00	10.20%	\$ 3,355,559.00
\$ 1,215,769.47	\$ 934,657.97	26.44%	\$ 3,382,873.00
\$ 90,302.00	\$ 87,177.00	1.24%	\$ 7,191,647.00
\$ 272,080.45	\$ 272,080.45	12.58%	\$ 1,890,888.00
\$ 130,500.00	\$ 62,500.00	8.15%	\$ 1,470,874.00
\$ 632,220.00	\$ 598,095.00	14.90%	\$ 3,611,089.00
\$ 1,910,910.00	\$ 1,445,350.00	19.02%	\$ 3,138,152.00
\$ 8,677,253.00	\$ 8,216,753.00	21.33%	\$ 12,010,958.00
\$ -	\$ -	0.00%	\$ -
\$ 5,708,133.65	\$ 4,747,063.65	23.59%	\$ 18,493,012.00
\$ -	\$ -	0.00%	\$ -
\$ -	\$ -	0.00%	\$ -
\$ 3,673,240.00	\$ 3,233,903.00	45.30%	\$ 4,436,342.00
\$ -	\$ -	0.00%	\$ 3,433,821.00
\$ -	\$ -	0.00%	\$ -
\$ 47,362,054.63	\$ 41,868,753.68	17.51%	\$ 223,082,801.00
\$ -	\$ -	0.00%	\$ -
\$ -	\$ -	0.00%	\$ -
\$ 47,362,054.63	\$ 41,868,753.68	18.18%	\$ 223,082,801.00
\$ 2,408,946.07	\$ 2,134,281.07	0.00%	\$ 2,408,946.07
\$ 44,953,108.56	\$ 39,734,472.61	17.51%	\$ 220,673,855.00
\$ 59,296.57	\$ 59,296.57	29.65%	\$ 140,703.00
\$ 122,037.00	\$ 116,387.00	22.56%	\$ 418,875.00
\$ 31,504.14	\$ 24,514.06	2.33%	\$ 1,318,496.00
\$ 212,837.71	\$ 200,197.63	10.18%	\$ 1,878,074.00
\$ -	\$ -	0.00%	\$ 6,112,825.00
\$ -	\$ -	0.00%	\$ 4,821,950.00
\$ -	\$ -	0.00%	\$ 10,934,775.00
\$ 72,725,253.82	\$ 66,976,245.85	22.56%	\$ 249,690,372.00
\$ 70,316,307.75	INVOICED NET (less retainage)		

Budget will be updated to \$381,967,231 once GMP is finalized and submitted to MSBA.

**Lowell HS Project
OPM Cashflow
April 2022**

<i>B</i>	<i>C</i>	<i>D</i>
Projected Date of Work (Exhibit D)	Projected Cost Monthly from Exhibit D of PS&B	Projected Cost Monthly (Updated Cashflow Apr 2022)
May-19	\$ 712,454	\$ -
June-19	\$ 750,904	\$ 407,223
July-19	\$ 818,624	\$ 674,620
August-19	\$ 863,399	\$ 920,300
September-19	\$ 846,349	\$ 1,009,885
October-19	\$ 893,649	\$ 884,028
November-19	\$ 900,015	\$ 764,140
December-19	\$ 872,165	\$ 756,230
January-20	\$ 901,374	\$ 785,526
February-20	\$ 912,902	\$ 786,615
March-20	\$ 914,519	\$ 880,727
April-20	\$ 904,947	\$ 924,230
May-20	\$ 903,956	\$ 878,611
June-20	\$ 897,027	\$ 892,855
July-20	\$ 1,173,236	\$ 911,279
August-20	\$ 1,012,994	\$ 982,408
September-20	\$ 988,005	\$ 932,342
October-20	\$ 1,275,565	\$ 1,732,989
November-20	\$ 1,015,622	\$ 1,546,781
December-20	\$ 2,100,587	\$ 1,590,952
January-21	\$ 2,331,843	\$ 1,465,536
February-21	\$ 2,245,675	\$ 1,755,309
March-21	\$ 2,446,474	\$ 2,563,808
April-21	\$ 2,712,592	\$ 2,058,828
May-21	\$ 2,638,200	\$ 2,136,545
June-21	\$ 2,825,089	\$ 3,575,177
July-21	\$ 4,476,482	\$ 1,413,899
August-21	\$ 3,080,231	\$ 3,393,938
September-21	\$ 3,148,540	\$ 1,915,465
October-21	\$ 3,177,369	\$ 4,686,799
November-21	\$ 3,153,344	\$ 3,243,221
December-21	\$ 3,103,243	\$ 3,120,749
January-22	\$ 3,023,250	\$ 5,530,518
February-22	\$ 2,894,206	\$ 3,824,699
March-22	\$ 2,652,449	\$ 5,474,343
April-22	\$ 2,444,390	\$ 3,806,362
May-22	\$ 2,195,402	\$ 5,292,812

**Lowell HS Project
OPM Cashflow
April 2022**

<i>B</i>	<i>C</i>	<i>D</i>
Projected Date of Work (Exhibit D)	Projected Cost Monthly from Exhibit D of PS&B	Projected Cost Monthly (Updated Cashflow Apr 2022)
June-22	\$ 3,524,399	\$ 4,533,209
July-22	\$ 7,040,516	\$ 6,144,739
August-22	\$ 8,191,852	\$ 3,806,357
September-22	\$ 7,075,053	\$ 1,789,818
October-22	\$ 7,676,842	\$ 1,817,430
November-22	\$ 7,997,478	\$ 2,514,438
December-22	\$ 8,086,194	\$ 3,571,736
January-23	\$ 7,897,567	\$ 5,962,103
February-23	\$ 7,556,144	\$ 9,120,967
March-23	\$ 7,034,672	\$ 9,652,171
April-23	\$ 6,402,645	\$ 10,014,178
May-23	\$ 5,684,556	\$ 5,179,496
June-23	\$ 4,919,889	\$ 5,567,479
July-23	\$ 4,157,702	\$ 5,864,890
August-23	\$ 3,418,326	\$ 7,761,800
September-23	\$ 2,750,814	\$ 4,789,460
October-23	\$ 2,194,644	\$ 4,359,420
November-23	\$ 3,397,045	\$ 4,882,766
December-23	\$ 3,181,990	\$ 6,495,200
January-24	\$ 1,866,507	\$ 5,669,762
February-24	\$ 2,642,978	\$ 5,374,622
March-24	\$ 3,282,033	\$ 5,727,591
April-24	\$ 3,850,550	\$ 5,949,642
May-24	\$ 4,123,744	\$ 6,607,846
June-24	\$ 4,339,260	\$ 6,960,929
July-24	\$ 4,495,718	\$ 6,146,105
August-24	\$ 4,706,498	\$ 7,255,489
September-24	\$ 4,844,696	\$ 6,517,254
October-24	\$ 4,919,830	\$ 5,883,842
November-24	\$ 4,912,711	\$ 6,080,674
December-24	\$ 4,832,888	\$ 4,709,398
January-25	\$ 4,680,353	\$ 4,782,842
February-25	\$ 4,455,123	\$ 4,273,724
March-25	\$ 4,174,638	\$ 3,182,329
April-25	\$ 3,812,443	\$ 3,652,522
May-25	\$ 3,369,433	\$ 3,579,690
June-25	\$ 4,350,331	\$ 4,640,539

**Lowell HS Project
OPM Cashflow
April 2022**

<i>B</i>	<i>C</i>	<i>D</i>
Projected Date of Work (Exhibit D)	Projected Cost Monthly from Exhibit D of PS&B	Projected Cost Monthly (Updated Cashflow Apr. 2022)
July-25	\$ 7,039,612	\$ 5,905,064
August-25	\$ 7,733,545	\$ 6,963,623
September-25	\$ 6,764,853	\$ 3,798,163
October-25	\$ 7,568,947	\$ 4,222,455
November-25	\$ 8,067,212	\$ 4,180,334
December-25	\$ 8,259,969	\$ 3,524,763
January-26	\$ 8,182,244	\$ 3,367,671
February-26	\$ 7,881,312	\$ 3,559,004
March-26	\$ 7,290,224	\$ 4,357,233
April-26	\$ 6,419,066	\$ 4,601,127
May-26	\$ 5,266,349	\$ 4,716,452
June-26	\$ 5,543,198	\$ 4,401,850
July-26	\$ 3,835,407	\$ 11,708,101
August-26	\$ 194,177	\$ 291,738
September-26	\$ 153,045	\$ 252,357
October-26	\$ 146,741	\$ 173,902
November-26	\$ 63,506	\$ 90,030
December-26	\$ 55,946	\$ 63,037
January-27	\$ 55,946	\$ 55,946
February-27	\$ 55,946	\$ 55,946
March-27	\$ 55,946	\$ 55,946
April-27	\$ 55,946	\$ 56,229
May-27	\$ 54,946	\$ 56,043
Total	\$ 340,799,217	\$ 340,799,217

[illegible]

[illegible]

LHS Project ProPay PTD – April 2022

Payment Request No	Request Type	Electronic Payment Request Date	Submitted Amount	Eligible Project Cost	Ineligible Project Cost	MSBA Payment Amount	MSBA Payment Date
<u>1</u>		8/18/2016	\$45,605	\$45,605	\$0	\$36,005	9/15/2016
<u>2</u>		12/29/2016	\$172,434	\$172,434	\$0	\$136,137	2/2/2017
<u>3</u>		3/10/2017	\$368,582	\$361,247	\$7,335	\$285,204	4/21/2017
<u>4</u>		7/18/2017	\$288,215	\$288,215	\$0	\$227,546	8/10/2017
<u>5</u>		1/5/2018	\$506,310	\$506,310	\$0	\$399,732	1/26/2018
<u>6</u>		5/18/2018	\$185,106	\$185,106	\$0	\$146,141	6/21/2018
<u>7</u>		10/4/2018	\$249,339	\$249,339	\$0	\$196,853	11/16/2018
<u>8</u>		3/4/2019	\$455,440	\$455,440	\$0	\$359,570	4/4/2019
<u>9</u>		6/12/2019	\$264,071	\$263,320	\$751	\$162,877	7/11/2019
<u>10</u>		10/21/2019	\$33,174	\$33,174	\$0	\$98,087	12/31/2020
<u>11</u>		12/18/2020	\$12,443,611	\$12,439,922	\$3,689	\$9,951,938	1/7/2021
<u>12</u>		2/10/2021	\$4,212,115	\$4,209,800	\$2,315	\$3,367,840	3/11/2021
<u>13</u>		3/31/2021	\$3,056,479	\$2,682,436	\$374,043	\$2,145,948	5/13/2021
<u>14</u>		5/19/2021	\$1,742,159	\$1,738,068	\$4,091	\$1,390,455	6/17/2021
<u>15</u>		7/9/2021	\$6,768,087	\$6,698,037	\$70,050	\$5,358,429	8/26/2021
<u>16</u>		8/10/2021	\$3,574,450	\$3,566,070	\$8,380	\$2,852,856	9/2/2021
<u>17</u>		10/6/2021	\$1,413,669	\$1,410,991	\$2,678	\$1,128,793	10/28/2021
<u>18</u>		1/10/2022	\$5,293,003	\$5,288,767	\$4,236	\$4,231,014	2/11/2022
<u>19</u>		2/17/2022	\$7,930,021	\$7,925,643	\$4,378	\$6,340,514	4/21/2022
<u>20</u>		4/15/2022	\$8,517,656	\$8,108,455	\$409,201	\$0	
Total			\$57,519,526	\$56,628,379	\$891,147	\$38,815,937	

PCO #	Title	Source Document	PCO Issue Date to Owner	Final Approval Date	CO #	BIC	Funding Source	Open/Closed/Void	Suffolk Submitted	Approved	Notes
001	Field Bulletin #1 - Gym Drain Line	FB 1	2/5/2021	4/26/2021	PGMP 4	Suffolk	PreGMP CO	Closed	\$ (6,312.00)	\$ (6,312.00)	Signed in DocUSign
002	Field Bulletin #5 - Foundation Modifications	FB 5R1	2/5/2021	7/12/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 61,532.00	\$ 52,373.00	Signed in DocUSign
003	Field Bulletin #4 - Steel Modifications	FB 4	2/5/2021	4/26/2021	PGMP 4	Suffolk	PreGMP CO	Closed	\$ 5,807.00	\$ 4,771.00	Signed in DocUSign
004	Void				VOID			VOID	\$ -	\$ -	
005	Snow Removal	N/A	1/28/2021	2/22/2021	N/A	Suffolk	Allowance	Closed	\$ 16,096.00	\$ 16,096.00	Signed in DocUSign
005.01	Snow Removal	N/A	3/26/2021		N/A	Suffolk	Allowance	Closed	\$ 4,145.00	\$ 4,145.00	Signed in DocUSign
005.02	Snow Removal - WLF -	CE 48	5/6/2021		N/A	Suffolk	Allowance	Closed	\$ 27,731.00	\$ 26,931.00	Signed in DocUSign
006	Down Time - Obstruction Removal	CE 32.3	1/28/2021	8/12/2021	PGMP 6	Suffolk	Allowance	Closed	\$ 350,000.00	\$ 297,354.00	Signed in DocUSign
006.01	Obstruction Removal - 1/9/21 to 1/30/21		5/20/2021		VOID			VOID	\$ -	\$ -	
006.02	Obstruction Removal - After 2/1/21		6/1/2021		VOID			VOID	\$ -	\$ -	
006.03	Premium Time - HUB	CE 32.3		8/11/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 2,923.00	\$ 2,923.00	Signed in DocUSign
007	Test Pit Work	CE 9.2	1/28/2021	3/23/2021	N/A	Suffolk	Allowance	Closed	\$ 4,613.00	\$ 4,613.00	Signed in DocUSign
007.01	Test Pit Work - Nobis Pre-Characterization 1/12/21 to 1/14/21	CE 9.2	3/1/2021	3/23/2021	N/A	Suffolk	Allowance	Closed	\$ 16,014.00	\$ 16,014.00	Signed in DocUSign
007.02	Test Pit Work - 2/4/21 to 2/8/21	CE 9.2			N/A	Suffolk	Allowance	Closed	\$ 14,162.00	\$ 14,162.00	Signed in DocUSign
008	Field Bulletin #9 - Geophysics Survey Gym	FB 9	1/28/2021	3/23/2021	N/A	Suffolk	Allowance	Closed	\$ 10,150.00	\$ 10,150.00	Signed in DocUSign
009	Addendum #3 - Additional RAPs	Addm 3	2/2/2021	2/16/2021	PGMP 4	Suffolk	PreGMP CO	Closed	\$ 72,265.00	\$ 72,265.00	Signed in DocUSign
010	Field Bulletin #3	FB 3	2/5/2021			Suffolk	PreGMP CO	Open	\$ 22,393.00	\$ 20,882.00	Signed in DocUSign
011	Field Bulletin #8 - Site Enabling Utility Plan - Proposal	FB 8		6/3/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ (5,927.00)	\$ (5,927.00)	Signed in DocUSign
011.01	Field Bulletin #8 - Site Enabling Utility Plan - T&M	FB 8	3/11/2021	4/26/2021	PGMP 4	Suffolk	PreGMP CO	Closed	\$ 34,998.00	\$ 34,998.00	Signed in DocUSign
012	Added WT / HSS Connections	RFI 039	2/24/2021	3/23/2021	PGMP 4	Suffolk	PreGMP CO	Closed	\$ 3,292.00	\$ 3,292.00	Signed in DocUSign
013	Abatement Scope Quantities	Specs	2/24/2021	3/23/2021		Suffolk	PreGMP CO	Open	\$ (7,962.00)	\$ (7,962.00)	Signed in DocUSign
014	Field Bulletin #14 - Site Coordination Civil	FB 14		6/7/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 5,667.00	\$ 5,667.00	Signed in DocUSign
015	WLF & JLM Working 10s and Saturdays	CE 44	5/3/2021		PGMP 5	Suffolk	PreGMP CO	Closed	\$ 3,122.00	\$ 3,122.00	Signed in DocUSign
015.01	Premium time	CE 44	4/29/2021	6/3/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 8,819.00	\$ 8,819.00	Signed in DocUSign
015.02	Premium Time - WLF - Saturday 02.27.21	CE 44	7/7/2021	7/29/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 4,432.00	\$ 4,432.00	Signed in DocUSign
016	Topsoil to Winchendon Landfill	CE 46.06			N/A	Suffolk	Allowance	Closed	\$ 63,239.00	\$ 63,239.00	Signed in DocUSign
016.01	Transportation of TCLP Soils	CE 46.06	3/11/2021		N/A	Suffolk	Allowance	Closed	\$ 70,445.00	\$ 70,445.00	Signed in DocUSign
016.02	Stockpile Management	CE 46.06	5/10/2021	8/23/2021	PGMP 6	Suffolk	Allowance	Closed	\$ 71,277.00	\$ 70,124.00	Signed in DocUSign
016.03	Soil Transportation to Winchendon	CE 46.06	6/10/2021	8/11/2021	PGMP 6	Suffolk	Allowance	Closed	\$ 107,790.00	\$ 107,790.00	Signed in DocUSign
016.04	Soil Transportation to Turnkey 3/24/21 to 3/25/21	CE 46.06	6/15/2021	7/29/2021	PGMP 6	Suffolk	Allowance	Closed	\$ 62,786.00	\$ 62,786.00	Signed in DocUSign
016.05	Soil Transportation to Winchendon 4/8/21 to 5/12/21	CE 46.06	6/15/2021	7/29/2021	PGMP 6	Suffolk	Allowance	Closed	\$ 50,730.00	\$ 50,730.00	Signed in DocUSign
016.06	Premium Cost for Soil Disposal at Winchendon Landfill	CE 46.06			N/A	Suffolk	Allowance	Closed	\$ 11,851.00	\$ 11,815.00	Signed in DocUSign
016.07	Soil Transportation to Winchendon 4/28 & 6/7/21 to 9/10/21	CE 046.07	10/19/2021	1/24/2022	PGMP 8	Suffolk	Allowance	Closed	\$ 35,429.00	\$ 35,429.00	Signed in DocUSign
016.8	Transportation and Disposal	CE 46.08	3/14/2022	3/30/2022	N/A	Suffolk	Allowance	Closed	\$ 3,375.00	\$ 3,375.00	Signed in DocUSign
017	Furish foundation sleeves	CE 51	3/11/2021	4/26/2021	PGMP 4	Suffolk	PreGMP CO	Closed	\$ 1,016.00	\$ 1,016.00	Signed in DocUSign
018	VOID				VOID			VOID			
019	Field Bulletin #13 - Asbestos Debris SMP	FB 13			VOID			VOID	\$ -	\$ -	
019A	Field Bulletin #13 - Asbestos Debris SMP	FB 13			PGMP 7	Suffolk	PreGMP CO	Closed	\$ 11,834.00	\$ 11,834.00	Signed in DocUSign
019B	Field Bulletin #13 - Asbestos Debris SMP	FB 13			PGMP 7	Suffolk	PreGMP CO	Closed	\$ (5,487.00)	\$ (5,487.00)	Signed in DocUSign
021	Repair Water Lateral & Pump Out Excavation	CE 57	4/1/2021		PGMP 5	Suffolk	PreGMP CO	Closed	\$ 34,382.00	\$ 34,382.00	Signed in DocUSign
22	Fall Protection Anchors	RFI 012R1	4/7/2021	12/21/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 32,744.00	\$ 4,668.00	Signed in DocUSign
023	Police Details - thru 3/31/2021	CE 48	4/1/2021	9/30/2021	N/A	Suffolk	Allowance	Closed	\$ 16,263.00	\$ 13,992.00	Signed in DocUSign
023.A	Police Detail - April 8th	CE 48A	11/3/2021	1/24/2022	N/A	Suffolk	Allowance	Closed	\$ 560.00	\$ 560.00	Signed in DocUSign
024	Winter Conditions -JLM through 3/10/2021	CE 32	4/7/2021		N/A	Suffolk	Allowance	Closed	\$ 25,728.00	\$ 25,128.00	Signed in DocUSign
024.01	Winter Conditions - JLM thru 03/31/2021	CE 32	4/29/2021		N/A	Suffolk	Allowance	Closed	\$ 17,523.00	\$ 17,523.00	Signed in DocUSign
024.02	Winter Conditions - WLF 2/5/2021 - 2/26/2021	CE 32	5/3/2021		N/A	Suffolk	Allowance	Closed	\$ 7,176.00	\$ 7,176.00	Signed in DocUSign
024.03	HUB snow removal & PT				VOID			VOID	\$ -	\$ -	
024.04	Winter Conditions - JLM 0 through 04.06.21	CE 32	7/7/2021		N/A	Suffolk	Allowance	Closed	\$ 10,566.00	\$ 10,556.00	Signed in DocUSign
024.05	Winter Conditions - WLF 4/21/21	CE 32.5	1/14/2022	2/14/2022	N/A	Suffolk	Allowance	Closed	\$ 1,979.00	\$ 1,979.00	Signed in DocUSign
025	5000psi Concrete Mix	CE 47	4/29/2021		N/A	Suffolk	Allowance	Closed	\$ 11,983.00	\$ 11,983.00	Signed in DocUSign
026	CE 45 - Gate Monitoring - 3/9/21 to 3/10/21		4/1/2021					VOID	\$ -	\$ -	
027	Deduct for multipoint connection pad	CE 49			PGMP 5	Suffolk	PreGMP CO	Closed	\$ (751.00)	\$ (751.00)	Signed in DocUSign
028	Credit for Damproofing Detail Clarification	RFI 047	4/8/2021	6/28/2021	PGMP 9	Suffolk	PreGMP CO	Closed	\$ (1,032.00)	\$ (1,032.00)	Signed in DocUSign
029	Field Bulletin 17 - Elevator and Steel Modifications	FB 17	5/10/2021	6/7/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 1,752.00	\$ 1,752.00	Signed in DocUSign
030	Revised Dunnage Steel Elevation	CE 63	5/10/2021		PGMP 7	Suffolk	PreGMP CO	Closed	\$ 2,434.00	\$ 1,335.00	Signed in DocUSign
031	Steel Revisions per Submittal Comments	CE 54	5/10/2021	5/13/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 9,127.00	\$ 9,127.00	Signed in DocUSign
032	Street Sweeping			6/28/2021	N/A	Suffolk	Allowance	Closed	\$ 1,719.00	\$ 1,719.00	Signed in DocUSign
033	Installation of Foundation Drain		5/27/2021	6/28/2021	PGMP 6	Suffolk	PreGMP CO	Closed	\$ 4,030.00	\$ 4,030.00	Signed in DocUSign
034	VOID				VOID			VOID			
035	Value Engineering				VOID			VOID	\$ -	\$ -	

PCO #	Title	Source Document	PCO Issue Date to Owner	Final Approval Date	CO #	BIC	Funding Source	Open/Closed/Void	Suffolk Submitted	Approved	Notes
036	Henry 795 in lieu of Henry 788		6/10/2021	6/28/2021	N/A	Suffolk	Allowance	Closed	\$ 617.00	\$ 561.00	Signed in DocUSign
037	Penthouse Columns		6/17/2021		PGMP 6	Suffolk	PreGMP CO	Closed	\$ 66,097.00	\$ 66,097.00	Signed in DocUSign
038	Concrete Pump Trucks		7/7/2021		PGMP 6	Suffolk	PreGMP CO	Closed	\$ 24,160.00	\$ 19,346.00	Signed in DocUSign
039	WLF Support for Zichelle Crane	CE 85	6/24/2021	3/30/2022	N/A	Suffolk	Allowance	Closed	\$ 10,255.00	\$ 10,255.00	Signed in DocUSign
040	Early Elevator Install - Steel	CE 95	7/9/2021	3/31/2022	PGMP 9	Suffolk	PreGMP CO	Open	\$ 109,857.00	\$ 109,118.00	Signed in DocUSign
041	Topping Off Ceremony & Fire Watches	CE 68	7/13/2021		N/A	Suffolk	Allowance	Closed	\$ 14,935.00	\$ 14,346.00	Signed in DocUSign
042	Part E service Area Modification	CE 91/FB 24	8/5/2021	5/11/2022		Suffolk	PreGMP CO	Open	\$ 57,126.00	\$ 61,054.00	Signed in DocUSign
043	Coordination - HVAC Equipment	CE 94/FB 28	8/5/2021		PGMP 7	Suffolk	PreGMP CO	Closed	\$ (1,783.00)	\$ (1,783.00)	Signed in DocUSign
044	Deletion of Kirk St Entry Canopy	CE 83/FB 20	2/3/2022	ON HOLD			PreGMP CO	Open	\$ 8,426.00	\$ -	Suffolk resubmitted 2/3/22
045	HVAC Value Management	CE 107/FB 30	8/12/2021	11/8/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (59,933.00)	\$ (59,933.00)	Signed in DocUSign
046	Architectural Value Management	CE 108/FB 31	8/25/2021	2/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ (245,060.00)	\$ (245,060.00)	Signed in DocUSign
047	CE 96 Added Paint Scope	CE 96	9/1/2021	1/24/2022	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 70,986.00	\$ 70,986.00	Signed in DocUSign
048	CE 74 Phase 1 Exterior Mock Up		9/1/2021	12/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 30,450.00	\$ 28,313.00	Signed in DocUSign
049	CE #112 FB #36 - HVAC Value Management Chiller	FB 36	9/2/2021		PGMP 7	Suffolk	PreGMP CO	Closed	\$ (25,500.00)	\$ (25,500.00)	Signed in DocUSign
050	Fire Wall	FB 21	9/17/2021	NEFS	HOT	PE	PreGMP CO	Open	\$ 44,973.00		
051	Gym Foundation Wall Crack	FB 18	9/17/2021	2/10/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 7,596.00	\$ 7,596.00	Signed in DocUSign
052	Metal Lockers	FB 27	9/17/2021	11/8/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (200,000.00)	\$ (200,000.00)	Signed in DocUSign
053	CE 131 - Arch VM - Toilet Partition Spec	FB 50	9/17/2021			Suffolk	PreGMP CO	Open	\$ (37,100.00)		Suff to revise & resubmit
054	CE 119 - Architectural VE Countertop Color	FB 39	10/21/2021	1/21/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ (35,575.00)	\$ (35,575.00)	Signed in DocUSign
055	Fire Sprinklers Above Cloud Ceilings in Building E	RFI 110	10/5/2021	11/8/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 14,896.00	\$ 14,437.00	Signed in DocUSign
056	CE 106 - Temp Transformer Pad		10/12/2021	10/27/2021	N/A	Suffolk	Allowance	Closed	\$ 2,658.00	\$ 2,479.00	Signed in DocUSign
057	CE 104 - 125 No Sprinklers Beneath Mechanical Mezzanine		10/14/2021	10/22/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 15,522.00	\$ 15,522.00	Signed in DocUSign
058	CE 168 - Installation of Door Frames at Masonry		10/12/2021	10/22/2021		Suffolk	PreGMP CO	Open	\$ 12,271.00	\$ 12,271.00	Signed in DocUSign
059	CE 093 - Mechanical DHW; Floor Drain & Vent Piping	RFI 89R1	10/14/2021	1/21/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 10,193.00	\$ 10,057.00	Signed in DocUSign
060	Electrical Coordination of DCU Equipment	FB 32	10/21/2021	2/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ (48,879.00)	\$ (50,749.00)	Signed in DocUSign
061	Electrical VE Items	FB 33	10/21/2021	1/24/2022	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (304,406.00)	\$ (304,406.00)	Signed in DocUSign
062	Grease ductwork & VAV Sound Attenuators VE Items	FB 38	10/21/2021	1/24/2022	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (18,150.00)	\$ (18,150.00)	Signed in DocUSign
063	Electrical Coordination for Elevator	FB 54	10/21/2021	1/24/2022	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (633.00)	\$ (944.00)	Signed in DocUSign
064	Electrical VE Items	FB 47	10/21/2021	11/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (75,830.00)	\$ (75,830.00)	Signed in DocUSign
065	Heat Trace Controllers	FB 57	10/21/2021	12/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 6,266.00	\$ 6,266.00	Signed in DocUSign
066	Electrical Coordination AHU & MAU	FB 67	10/21/2021	12/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ (225.00)	\$ (225.00)	Signed in DocUSign
067	Electrical Coordination with Elevators	FB 69	10/21/2021	12/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 3,429.00	\$ 3,429.00	Signed in DocUSign
068	Added Custodian Outlets	FB 61	10/21/2021	11/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 3,869.00	\$ 3,869.00	Signed in DocUSign
069	Part E Ceiling Clarification	FB 58	10/27/2021	12/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 118,851.00	\$ 118,851.00	Signed in DocUSign
070	24" Drain Conflict with Existing Gas Line & Duct Bank on A	RFI 081	10/27/2021	12/15/2021	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 35,298.00	\$ 35,298.00	Signed in DocUSign
071	Disinfecting for Positive COVID-19 Case		11/3/2022				PreGMP CO	Void	\$ 2,797.00		
072	Electrical Coordination with DCUs	FB 065	11/3/2021	2/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 7,508.00	\$ 8,321.00	Signed in DocUSign
073	RFI 146: PE2 Elevator Control Room Changes	CE 135	12/1/2021	2/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 951.00	\$ 951.00	Signed in DocUSign
074	Motorized Shades	FB 29	11/10/2021	1/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 134.00	\$ 134.00	Signed in DocUSign
075	Coordination with Food Service Equipment	FB 64	11/10/2021	3/22/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ (494.00)	\$ 494.00	Signed in DocUSign
076	Arch Value Management - Wall Tile Detail	FB 51	1/20/2022	3/22/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ (68,981.00)	\$ (68,981.00)	Signed in DocUSign
077	NEFS Premium Time at North Elevation	CE 150	12/1/2021	1/12/2022	PGMP 8	Suffolk	PreGMP CO	Closed	\$ 12,907.00	\$ 12,907.00	Signed in DocUSign
078	Part E Relocation of Girt	FB 49	12/9/2021	2/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 15,001.00	\$ 15,001.00	Signed in DocUSign
079	Trainer Room Ice Maker	FB 45	12/8/2021	4/27/2022		Suffolk	PreGMP CO	Open	\$ 6,673.00	\$ 6,673.00	Signed in DocUSign
080	5/13/22 Not yet issued										
081	RFI 121: Building C 3rd Floor Electrical Demo	CE 120	12/10/2021	5/11/2022		Suffolk	PreGMP CO	Open	\$ 3,875.00	\$ 3,875.00	Signed in DocUSign
082	Added Data in Office	FB 71	2/3/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 20,636.00	\$ 18,181.00	Signed in DocUSign
083	Trainers Room Ceiling	FB 48/CE 176	12/15/2021	2/14/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 8,393.00	\$ 11,938.00	Signed in DocUSign
084	5/13/22 Not yet issued										
085	5/13/22 Not yet issued										
086	Premium Time - WJ Griffin	CE 044.3	1/11/2022		HOT	Suffolk	CM Construction Contin	Open	\$ 4,789.00		Pending Revised Griffin Rates
087	Downtime due to Site Limitations		12/17/2021	3/22/2022		Suffolk	PreGMP CO	Open	\$ 3,724.00	\$ 3,724.00	Signed in DocUSign
088	5/13/22 Not yet issued										
089	Field Bulletin 018 Foundation Repair		12/22/2021	2/10/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 3,261.00	\$ 3,261.00	Signed in DocUSign
090	SAN SWR Invert Change	RFI 105	1/6/2022			PE	PreGMP CO	Open	\$ 13,165.00	\$ 14,094.45	
091	WLF Rent Laborer to Suffolk on 5/13/21 & 5/22/21		1/14/2022	3/30/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 1,567.00	\$ 707.00	Signed in DocUSign
092	Flooring Modification @ Strength Room C1014	FB 66	1/24/2022				PreGMP CO	Void	\$ 58,512.00		Declined by Owner
093	WLF Obstruction Removal 6.15.21		1/27/2022	1/24/2022		Suffolk	PreGMP CO	Open	\$ 1,125.00	\$ 1,125.00	Signed in DocUSign
094	SDS Door Caulking Removal - 1980's Bldg	CE 262	1/27/2022	3/30/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 1,104.00	\$ 1,104.00	Signed in DocUSign
095	RFI 098 / Electrical Chase at Levels 1 & 2	CE 97	1/31/2022			Suffolk	PreGMP CO	Open	\$ 27,647.00		Suff to revise & resubmit

PCO #	Title	Source Document	PCO Issue Date to Owner	Final Approval Date	CO #	BIC	Funding Source	Open/Closed/Void	Suffolk Submitted	Approved	Notes
096	Overhead Gym Equipment Redesign Costs	CE 268	3/17/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 19,140.00	\$ 10,670.00	Signed in DocUSign
097	Re-cut Shaft Opening at Elevator Shaft - 1980s Building	CE 275	2/1/2022	3/22/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 1,589.00	\$ 1,589.00	Signed in DocUSign
098	Gym Equipment Controls	FB 109	2/3/2022	1/24/2022	PGMP 9	Suffolk	PreGMP CO	Closed	\$ 9,384.00	\$ 9,384.00	Signed in DocUSign
099	Building C - Room 423 - Two Added Duplex Units		2/7/2022			Suffolk	PreGMP CO	Open	\$ 2,387.00		Suff to revise & resubmit
100	Structural Modification Part C		2/7/2022			PE	PreGMP CO	Open	\$ 1,224.00		
101	Drinking Fountain	FB52	2/8/2022			PE	PreGMP CO	Open	\$ 353.00		
102	Homer PT Work - Building C		2/8/2022	4/22/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 516.00	\$ 516.00	Signed in DocUSign
103	PE3 Elevator Pit Concrete Pour - Premium Time	CE 279	3/1/2022	5/11/2022	N/A	Suffolk	Owner Construction Co	Closed	\$ 2,025.00	\$ 2,025.00	Signed in DocUSign
104	Misssing Footing for Gym Stair	CE 143	2/15/2022			Suffolk	PreGMP CO	Open	\$ 6,408.00		Suff to revise & resubmit
105	Phase 1 HM Modifications	CE 137 / FB 44	2/15/2022			Suffolk	PreGMP CO	Open	\$ 4,373.00	\$ 4,373.00	Suff to clarify item 2
106	Temp Conditions at Building C Elevator	CE 122	2/15/2022			Skanska	CM Construction Contin	Open	\$ 340.00		Suffolk resubmitted 5/10/22
107	Architectural VM	FB055	2/16/2022			Skanska	PreGMP CO	Open	\$ (7,068.00)		5/6 LC comments to KK
108	5/13/22 Not Yet Issued										
109	Drilled Micropiles Obstructions	CE 211	4/20/2022	5/11/2022	N/A	Suffolk	Allowance	Closed	\$ 14,720.00	\$ 14,720.00	Signed in DocUSign
110	Replacement Handle for Building C Office	CE 294	2/23/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 256.00	\$ 256.00	Signed in DocUSign
111	Field Office Relocation from Pool House	CE 067	2/23/2022	5/11/2022	N/A	Suffolk	Allowance	Closed	\$ 9,570.00	\$ 13,558.00	Signed in DocUSign
112	Concrete Wash Out on 9.22.21	CE 167	2/24/2022			Suffolk	Allowance	Open	\$ 1,915.00		
113	Street Sweeping After Concrete Pour 7/30/21	CE 61.1	3/1/2022	3/25/2022	N/A	Suffolk	Allowance	Closed	\$ 573.00	\$ 573.00	Signed in DocUSign
114	5/13/22 Not Yet Issued										
115	JLM Premium Time Only Work on 8/25/21 & 8/28/21	CE 295	3/1/2022	4/22/2022	N/A	Suffolk	Owner Construction Co	Closed	\$ 898.00	\$ 898.00	Signed in DocUSign
116	City of Lowell Public Safety System	CE 23 / FB 97	3/1/2022	3/25/2022	PGMP 9	Suffolk	PreGMP CO	Open	\$ 41,634.00	\$ 37,620.00	Signed in DocUSign
117	Test Pit to Locate Duct Bank per RFI 81	CE 009.3	3/1/2022	ON HOLD			Allowance	Open	\$ 2,455.00		
118	Arch Value Management - Casework	FB 56	3/2/2022	4/27/2022		Suffolk	PreGMP CO	Open	\$ (136,887.00)	\$ (136,887.00)	Signed in DocUSign
119	Exposed Steel Pre Prime Clarification - Bldg E	CE 274	3/7/2022			Skanska	PreGMP CO	Open	\$ 5,696.00		
120	HVAC VM PVC Covering & Condensate Drain Lines	FB 122	3/4/2022			Suffolk	PreGMP CO	Open	\$ 164,148.00	\$ 164,148.00	Suffolk to send in DocuSign
121	Phase 1 Exterior Light Pole Bases	CE 148	3/7/2022	WL French	HOT	Suffolk	PreGMP CO	Open	\$ 74,519.00		Suff to revise & resubmit
122	Electrical Rough for HRC	CE 147	3/8/2022			PE	PreGMP CO	Open	\$ 40,012.00		Revision required or Void per KK 5/6
123	Electrical Excavation & Backfill by WL French on East Side	CE 146	3/17/2022				PreGMP CO	Void	\$ 33,550.00		Voided 4/18/22
124	Hand Dryer Credit	CE 306	3/8/2022			PE	PreGMP CO	Open	\$ (8,000.00)		Suff to revise & resubmit
125	Hose Bibb	CE 185 / FB 70	3/9/2022			Skanska	PreGMP CO	Open	\$ 5,114.00		
126	Relocate Floor Drain for Recessed Slab	CE 166	3/9/2022	4/27/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 11,920.00	\$ 11,920.00	Signed in DocUSign
127	Roof Blocking	CE 161	3/9/2022	3/31/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 16,632.00	\$ 16,632.00	Signed in DocUSign
128	PE2 Elevator Pit & Shaft Dimensions	CE 152	3/9/2022			Skanska	PreGMP CO	Open	\$ 4,824.00		
129	Premium Time - W.L. French	CE 322	3/14/2022	4/27/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 1,539.00	\$ 1,539.00	Signed in DocUSign
130	Additional Door Lock Hardware for Closets in C Building	CE 324	3/14/2022	NEFS	HOT	Suffolk	PreGMP CO	Open	\$ 1,077.00	\$ 1,077.00	Suff to revise & resubmit
131	Fire Protection Main Relocation	RFI 376	3/14/2022				PreGMP CO	Void	\$ 8,910.00		Rejected - out of scope change
132	Truss System / Curtainwall	CE 325/RFI 195	4/21/2022			PE	PreGMP CO	Open	\$ 1,495.63		Rejected by Skanska
133	Select Demo - 12/26/21	CE 44.04	3/15/2022	4/27/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 1,294.00	\$ 1,294.00	Signed in DocUSign
134	Trimming Gusset Plate	CE 326	3/15/2022			PE	PreGMP CO	Open	\$ 844.00	\$ 844.00	
135	Delete Temp TV Studio	FB 022	3/18/2022			PE	PreGMP CO	Open	\$ (313,325.00)		Suff to revise & resubmit
136	Floor Sleeve Adapters for Volleyball Sleeves	CE 317	4/18/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 2,750.00	\$ 2,750.00	Signed in DocUSign
137	Slab Clarifications	FB 68	3/31/2022			Skanska	PreGMP CO	Open	\$ 9,473.00		
138	Wall Tile - Building E	CE 187 / RFI 23	4/1/2022		HOT	Suffolk	PreGMP CO	Open	\$ 6,617.00		5/6 Suff to resubmit w/ addtl info
139	Blocking for Toilet Partitions	CE 190 / FB 77	4/2/2022			Skanska	PreGMP CO	Open	\$ 6,773.00		
140	Elec-HVAC Coord - East Building Penthouse Louver	CE 191 / FB 78	4/2/2022			Suffolk	PreGMP CO	Open	\$ 724.00	\$ 724.00	Suffolk to send in DocuSign
141	Non-Shrink Grout per FBRA Report 16, Item #3	CE 192	4/2/2022			Suffolk	CM Construction Contin	Open	\$ 760.00	\$ 760.00	Suffolk to send in DocuSign
142	Sprinklers West Lightwells	CE 194 / FB 53	4/5/2022			Suffolk	PreGMP CO	Open	\$ 15,479.00	\$ 15,479.00	Suff to revise & resubmit
143	TWC PT - 10.2.21 Waterproofing South Wall	CE 44.05	4/5/2022	4/27/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 726.00	\$ 726.00	Signed in DocUSign
144	Electrical Room C1021E Drip Pan	RFI 468	4/5/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 8,998.00	\$ 8,998.00	Signed in DocUSign
145	5/13/22 Not Yet Issued										
146	Switchgear Manhole Relocation	CE 202	4/11/2022	5/13/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 14,268.00	\$ 14,268.00	Signed in DocUSign
147	Weather Protection - NEFS	CE 208	4/12/2022	4/27/2022	N/A	Suffolk	Allowance	Closed	\$ 41,674.00	\$ 43,197.00	Signed in DocUSign
148	Change in Wallboard Type from X to MR	CE 359	4/13/2022	4/27/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 1,397.00	\$ 1,397.00	Signed in DocUSign
149	Babfar Connections	CE 197	4/19/2022		HOT	Skanska	Allowance	Open	\$ 10,898.00		Part 1 of 2; # 2 to follow per Tyler
150	5/13/22 Not Yet Issued										
151	Soffit at Doors North Elevation	CE 207/FB 75	4/19/2022			Skanska	PreGMP CO	Open	\$ 3,781.36		
152	5/13/22 Not Yet Issued										
153	Ceiling Transition at GWB & Tectum to Radiant Panels	CE 321/RFI 433	4/21/2022			PE	PreGMP CO	Open	\$ 8,492.00		Rejected by Skanska
154	5/13/22 Not Yet Issued										
155	Expose Brick Shelf for Waterproofing	CE 160	4/27/2022	5/11/2022	N/A	Suffolk	CM Construction Contin	Closed	\$ 895.00	\$ 895.00	Signed in DocUSign



Print Date: 5/13/2022

PCO #	Title	Source Document	PCO Issue Date to Owner	Final Approval Date	CO #	BIC	Funding Source	Open/Closed/Void	Suffolk Submitted	Approved	Notes	
156	Temp Security Desk	FB93/CE281	4/27/2022			PE	PreGMP CO	Open	\$ 43,498.48		Suff to revise & resubmit	
157	Generator Room C3001 Fire Dampers	CE 368/RFI 434	4/27/2022			PE	PreGMP CO	Open	\$ 7,482.42	\$ 7,482.42		
158	Verizon Conduit	FB95/CE 319	4/27/2022			Skanska	PreGMP CO	Open	\$ 89,457.19			
159	Hollow Metal Frames Type Change at Multipurpose Entry	RFI 234	4/27/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 1,397.00	\$ 1,397.00	Signed in DocUSign	
160	VOID							Void				
161	Christmas Break Enabling Work - NEFS	CE 223.01	5/2/2022	5/11/2022		Suffolk	PreGMP CO	Open	\$ 13,901.00	\$ 13,901.00	Signed in DocUSign	
162	5/13/22 Not Yet Issued											
163	5/13/22 Not Yet Issued											
164	Heat Trace	CE 215 / FB 88	5/3/2022			Skanska	PreGMP CO	Open	\$ 28,012.25			
165	Electrical Security Coordination	CE 216/FB 89	5/3/2022			Skanska	PreGMP CO	Open	\$ (211.26)			
166	Bldg C Little Theater Rooftop Feeder	CE 212	5/4/2022			Skanska	PreGMP CO	Open	\$ 2,263.25			
167	5/13/22 Not Yet Issued											
168	Additional Loose Stone for the Site	CE 227	5/10/2022		HOT	PE	Allowance	Open	\$ 4,381.00	\$ 4,381.00		
TBD	Credit from Cives for Beam Pens											
	Field Bulletin #2 - Sinkhole and Existing Foundations	FB 2						Void	\$ -	\$ -	Proceed on T&M eMail from Vinny on 1/	
	Field Bulletin #7 - Updated Site Survey	FB 7						Void	\$ -	\$ -		
TBD	Credit from French for Temp access between Dutton & existing loading dock											
									\$ -	\$ -		
